STATE OF COLORADO

Bilobran - CDOT, Timothy <timothy.bilobran@state.co.us>

Re: FW: CEMEX TIS - Final

1 message


Bilobran - CDOT, Timothy <timothy.bilobran@state.co.us> Fri, Sep 8, 2023 at 1:26 PM
To: John V Heffernan <johnv.heffernan@cemex.com>

Afternoon John,

I read through the study today. I'm going to start this email with a note of appreciation that your company seemingly acted with Integrity here with your declarations. There's a lot of gray area in traffic engineering that allows for studies to be nudged to certain outcomes. When I read through the Stantec disclaimer at the beginning (which was far and away the lengthiest and most legal I've ever read in my 18-year career), I felt apprehensive about what I was about to read, especially since some level of the data collection pre2023 hinged on your company truthfully disclosing your traffic volumes to Stantec. All in all though it seems like a fairly well put together study.


The study makes it clear though that we're well past the 20% threshold traffic increase to require a new permit under the Colorado Access Code:

"

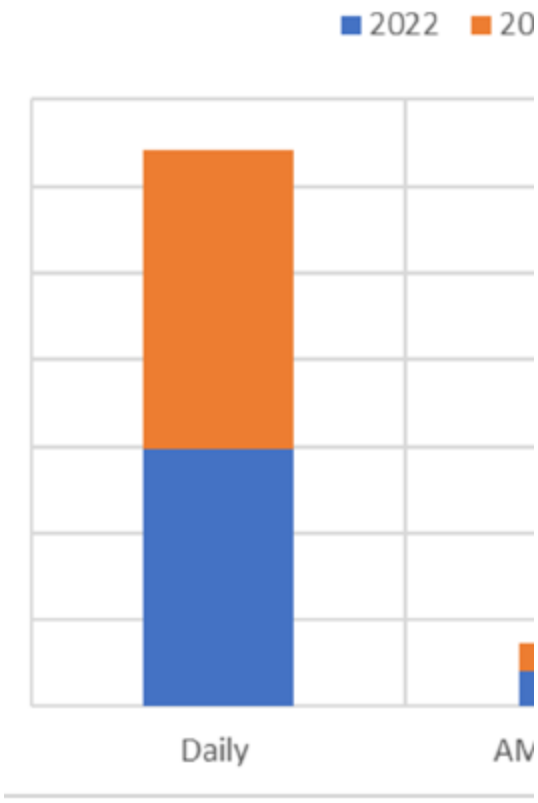

Since new permits are required from this office, part of the terms of the Highway 66 ACP & accompanying Intergovernmental Agreement, the associated access points need to come into conformance with the Highway 66 Access Control Plan:



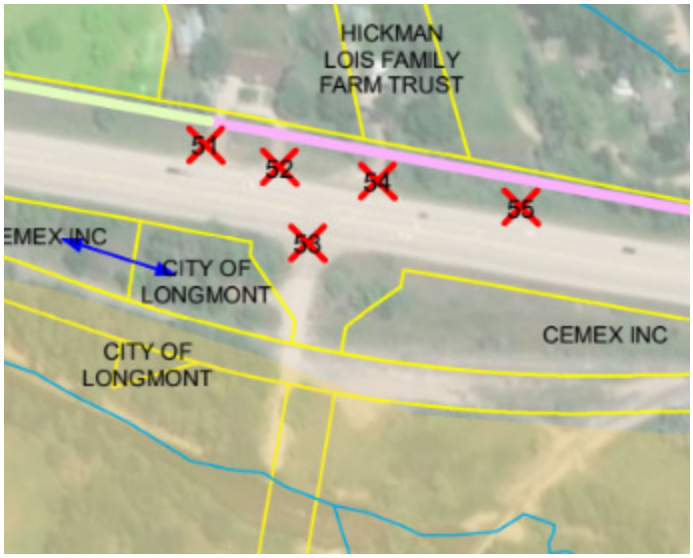

Number 49 language necessitating the change to a 3/4 movement.

						Access to the property will be obtained via Access 47.
29.376	49	South	Private Drive	Full Movement (Unsignalized)	**3/4 Movement**	Access will be restricted to less than full movement if a raised median is added to SH 66 as part of a roadway improvement project, if the property redevelops, or if operational and/or safety issues are identified through the completion of a traffic study.

Number 53 language necessitating the access closure.

29.466	53	South	51st St	Full Movement (Unsignalized)	**Access to be closed**	Access to properties south of SH 66 has been relocated to Access 49. This access will be formally closed and access will be obtained from existing Access 49.
						Access will be restricted to less than full movement if a raised median is


Vehicles will no longer be able to turn left out of access point 49 in these documents. for next steps we need to talk about what roadway construction needs to happen but before we do, I have a few more follow-up questions on the traffic study:

1. For access point 49, the study needs to state whether the eastbound right turn deceleration lane meets the length required under the Access Code. Note they need to use the Access Code Length and not AASHTO's length. The Access Code length is typically longer than AASHTO for these auxiliary safety lanes.
2. You'll need to have an internal discussion on westbound hauling routes. The study states that there may be alternative routes conceivably directly to Highway 66. The study will need to be updated to address any westbound turning movements exiting your facility and how those movements are reaching the state highway system, whether that's a direct access on Highway 66 or simple "Nascar Rights" using blocks of county roads.

> Another possible mitigation measure for the SH 66 & CEMEX Driveway intersection is to prohibit northbound left-turns and develop an alternate route along SH 66, west of the cement plant. Lastly,

I've hopefully laid out all the facts as succinctly as possible here. If you would like to still talk on the phone, I will copy and paste my schedule below. Simply send me a calendar invitation with your preferred video platform for whatever day and

time combination works for your calendar and mine.

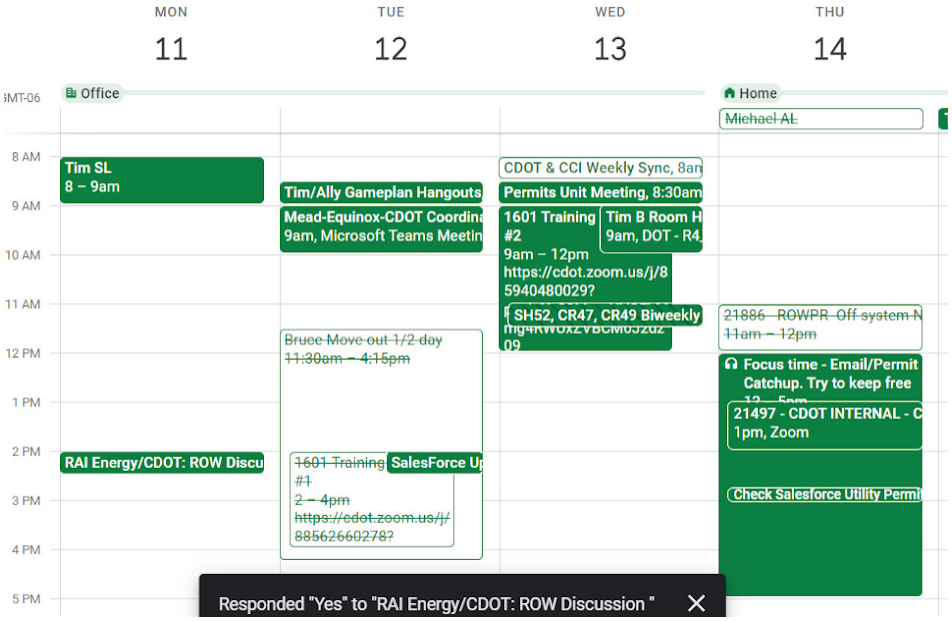

Thanks,
Tim
970-302-4022

On Fri, Sep 1, 2023 at 12:01 PM John V Heffernan <johnv.heffernan@cemex.com> wrote:

> Tim,
>
> Please see attached Traffic Study, and let me know if you have any questions or want to discuss.
>
> Thanks, and have a good Labor Day Weekend,
>
> John
>
> John Heffernan
>
> 713-722-6078 (office)
>
> 678-591-2925 (mobile)
>
> ---
>
> **From:** Hypnarowski, Brent <Brent.Hypnarowski@stantec.com>
> **Sent:** Friday, September 1, 2023 11:49 AM
> **To:** John V Heffernan <johnv.heffernan@cemex.com>
> **Subject:** CEMEX TIS - Final
>
> Hi John,

CAUTION: External Email | PRECAUCIÓN: Correo electrónico externo | VORSICHT: Externe E-Mail | ATTENTION: Courriel externe To learn more about email protection click here

I have attached the final, stamped version of the CEMEX Lyons Access Traffic Impact Study.

I appreciate all of your input and coordination throughout the duration of the study. It was a pleasure working with you and your team. Thank you for putting your trust in Stantec.

Best of luck with the rest of the process. Please do not hesitate to reach out if there is anything else that we can do for you.

Regards,

Brent Hypnarowski PE
Traffic Engineer

Stantec Consulting Services Inc.
410 17th Street, Suite 1400
Denver, CO 80202

Direct: (303) 285-4532



CONFIDENTIALITY: The information contained in this transmission may contain privileged and confidential information. It is intended only for the use of the person(s) named above. If you are not the intended recipient, you are hereby notified that any review, dissemination, distribution or duplication of this communication, and the information contained in it, is strictly prohibited. If you are not the intended recipient, please contact the sender and immediately destroy all copies of the original message.

--

Tim Bilobran
Region 4 Permits Manager



O 970.350.2163 | C 970.302.4022 | F 970.350.2198
timothy.bilobran@state.co.us | **codot.gov** | **www.cotrip.org**
10601 W. 10th Street, Greeley, CO 80634
